

**ROLLERI
EXCAVATION INC.**

P.O. Box 1208
Altaville, CA 95221



Page 1 of 2



Bryan Roller
Phone #: 209-736-9409

bryanrolleri@yahoo.com
NAWT Inspector ID #11466ITC

Septic Inspection Report


Buyer: N/A Realtor: N/A
Property Owner: N/A Realtor: Chase International Real Estate
Property Address: 7230 Latigo Street, Angels Camp
A.P.N.: 052-011-002
Inspection Date: 3-30-26 Year Built: 1979

Number of Bedrooms in Dwelling: 2
Water Source: X Well Community Other

Type of System

- ☒ Standard Gravity
☐ Pump to Gravity
☐ Pressure Dose
☐ Sand Filter
☐ Advantex
☐ Pressurized mound system
☐ Holding Tank
Other (describe)

Approximate Septic Tank and Leach Field Location

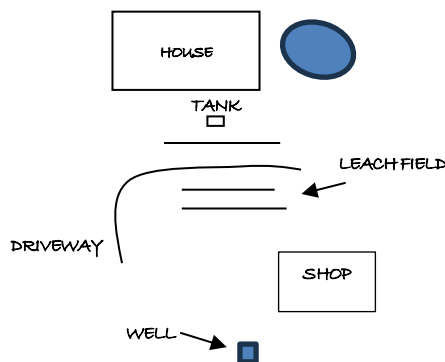

Septic Tank(s)

Septic Tank Type: ☒ Concrete ☐ Poly ☐ Fiberglass
Septic Tank Size: ☐ Approx. 1,000-1,200 Gallons ☒ Approx. 1,500 Gallons
Dosing Tank Type: ☐ Concrete ☐ Poly ☐ Fiberglass
Dosing Tank Size: ☐ Approx. 300-400 Gallons

Comments on Septic Tank: The tank was pumped on 3-30-26. The tank has approx. 7' of fill dirt on top of it. The depth was too deep to inspect the inside of the tank.

Distance from Septic Tank to Well: 100+

Page 2 of 2

Observations

- ☐ The tank(s) were not pumped.
- ☐ The tank(s) have been pumped and were physically entered and were completely inspected and is/are free of any structural defects and are functioning properly.
- ☒ The tank(s) were pumped but not entered and appear to be functioning properly.
- ☐ The tank(s) and drain field inspection revealed the following:

Determinations

☒ A visual inspection indicates no evidence of system failure. The system has passed the water load test properly and is approved for current use.

☐ A visual inspection indicates the system is functioning and passed the water load test. The tank needs to be pumped. A pumping company will need to be contacted to make further arrangements. Please notify us with the pumping date. We will return after the tank has been pumped to inspect the integrity of it.

☐ A visual inspection indicates that the system has failed the water load test. A further investigation is needed.

Certification

The undersigned cannot guarantee the continued acceptability of the private sewage disposal system due to unpredictable factors, which could later determine the life or code compliance of the system.

Bryan Rolleri

Inspector's Signature

11466ITC

Inspector ID #
